



Monthly Progress Report

**Sherburne-Earlville Central School District
2022 Capital Project**

To: Robert Berson, Superintendent
Joanne Palamaro, Director of Finance and Personnel
Ben Lewis, Coordinator of Transportation and Maintenance

Report Number #1

Week Ending: June 28, 2024

From: Evan Rivers, Schoolhouse Construction
Tim Scoones, Schoolhouse Construction

Carbon Copy: Robert Kernan, The LA Group
David Funk, Ashley McGraw

SED Control #: 08-20-01-04-0-012-013

Summary

Clark Companies arrived onsite and began work on Monday June 3rd. Within the first month of site work, Clark has been successful with scheduled progress made. The bulleted items listed below represent the work Clark has completed and/or is in progress currently.

Athletic Field

- Existing Topsoil stripped and removed off-site.
- Field Goal Posts removed for reuse.
- Existing Scoreboard and steel I-Beams removed for reuse.
- Pre-Existing irrigation system, piping, and wiring removed.
- Subgrade brought to new grade.
- Perimeter storm drainage installed.
- Partial conduit runs for the new scoreboard and game clock installed.
- Proof Rolling
- Pole Vault, High Jump, and Long Jump areas removed.
- New Scoreboard and game clock location determined.

Summary Continued

Track Area

- Pre-Existing track surfaced removed.
- Pre-Existing track base milled. (Millings saved for fill)
- Compaction and proof-roll testing.
- Asphalt walkway and wood timbers removed.
- Proof Rolling

Outer Area

- Construction perimeter fencing installed with signage.
- Silt fence installation.
- 4 Ft perimeter track fencing removed.
- Section of 8ft perimeter fencing removed.
- Topsoil stripped on East hill, Field Goal areas, and North and South ends of grandstands.
- The storage building next to the concession stand was safely removed and stored for reuse.
- Concrete slab from the storage building removed.
- Concrete walk on south end of grandstands removed.
- East Side Bleachers relocated and stored for reuse.
- Elevation brought up on east hill.

Project Challenges

- Field Infiltration
 - On Thursday June 20th, Firefly Sports Testing was onsite to conduct the required infiltration tests on the subgrade. It was discovered that the fields current infiltration rates did not meet the required range. Currently Schoolhouse is working with The LA Group, Clark, and Firefly Testing to create an alteration in field subgrade drainage that will accommodate the specifications.
- Existing Track Subgrade Conditions.
 - On Wednesday June 27th, Atlantic Testing Laboratories (ATL) was onsite with Schoolhouse and Clark to observe a proof-roll of the field and track subgrade. Concluding the proof-roll it was determined that there are significant areas that do not meet standards for Clark to continue with fine grading and install. Schoolhouse, The LA Group, and Clark are currently working to remove the unsuitable soils in these areas, and recompact the newly imported structural fill.

Field Progress Photos



Construction Zone Perimeter Fencing



Athletic Field Top Soil Ripping



Outer Area Top Soil Ripping



Track Milling

Field Progress Photos Continued



Track Subgrade Prep



Perimeter Storm Drainage Install



Subgrade Fine Grading




Field Subgrade Infiltration Testing

Field Progress Photos Continued



Storm Drainage and Conduit Install

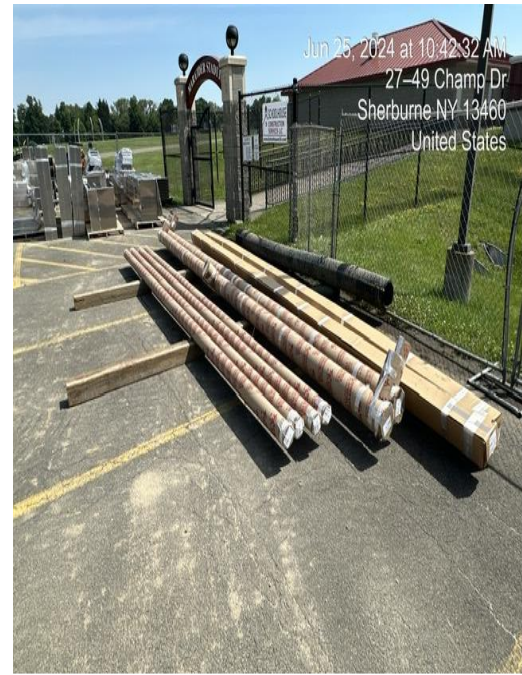

New Field Equipment Arrive Onsite



Storage Building Removed for Reuse



Current View of Construction
