



20850 State Highway 28  
Delhi, NY 13753



# Monthly Progress Report

Sherburne-Earlville Central School District  
2022 Capital Project

To: Robert Berson, Superintendent  
Joanne Palamaro, Director of Finance and Personnel  
Ben Lewis, Coordinator of Transportation and  
Maintenance  
From: Evan Rivers, Schoolhouse Construction  
Tim Scoones Schoolhouse Construction

Report Number #3  
Week Ending: August 30, 2024  
Carbon Copy: Robert Kernan, The LA Group  
David Funk, Ashley McGraw

SED Control #: 08-20-01-04-0-012-013

## Summary

Contractors working onsite had a very productive month throughout August. Many visual changes to the Track, Field, and surrounding areas took place. Clark Companies continued to work with drainage around outer areas of the track and throwing areas. Many of Clark’s subcontractors, such as Chenango Contracting (Turf Installer) and Davis Wallbridge Paving were onsite as well. Onsite construction meetings were held throughout the month discussing progress and the District, Schoolhouse Construction, The L.A. Group, and Clark Companies were all in attendance.

## Capital Improvement Project - Phase II Status

On August 5<sup>th</sup>, 2024, Sherburne Earlville Central School District awarded construction contracts to proceed with Phase 2 of the 2022 Capital Improvement Project. Starting Monday September 9<sup>th</sup>, 2024, contractors will arrive on-site to begin construction in the MS/HS Auditorium and Locker Rooms. A portion of this phase includes the construction of a new playground for the Elementary School which is currently underway. Temporary fencing and signage for construction material layout has been placed in designated areas.

## Turf Field Progress Details

### Athletic Field

- Finish Stone was string-lined to identify any high/low areas.
- Synthetic Turf was delivered, laid out and sewn together.
- Field markings, lines, and logos were cut out and designated synthetic turf colors glued in.
- Both D-Zones were paved.
- Field Sand, Rubber, and equipment were delivered.

### Track Area

- All concrete sidewalks, curbs, and walkways were poured and finished.
- ATL onsite for continued concrete testing throughout pours.
- Subgrade was brought up to final grade elevation and compacted.
- Asphalt paving around the track, A binder course and a fine course were installed.
- ATL onsite for paving testing.
- Fencing Contractors core-drilled holes in concrete sidewalks and installed fence posts.

### Outer Area

- Continued stormwater drainage installations.
- Stormwater catch basins, and hydrodynamic separator installed.
- Concrete sidewalk poured.
- Shot Put and Discus throwing areas graded, formed, and concrete poured.
- Post Sleeves for Discus caged set and poured.
- Drainage in throwing areas installed and connected to 12" stormwater drainage.
- Final grading continued East Side of construction area.
- Steel I-Beams for new scoreboard installed and set in concrete.

### Project Challenges

- Unknown Underground Electric
  - Throughout continued excavation for drainage in the outer areas of the track, Clark continued to find underground electric that was not expected. Clark continued to work around existing electric leaving it undisturbed and in place.
- Weather
  - August brought continued periods of rain that made concrete work, fine grading, and other installations difficult to work around.


**Field Progress Photos**



*Discus Cage Sleeve Pours*



*Concrete Sidewalk Forms and Reinforcement*

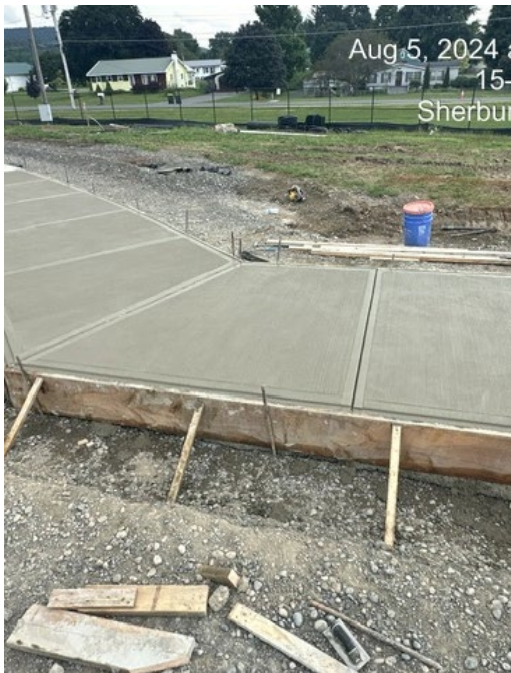

*New Concrete Sidewalk*



*Final Subgrade Grading*

## Field Progress Photos Continued



*Stormwater Drainage Installation*



*ATL On-site Testing Concrete*



*New Scoreboard Steel I-Beams*




*Track Asphalt Paving Began*

## Field Progress Photos Continued




*Top Course Asphalt Paving*

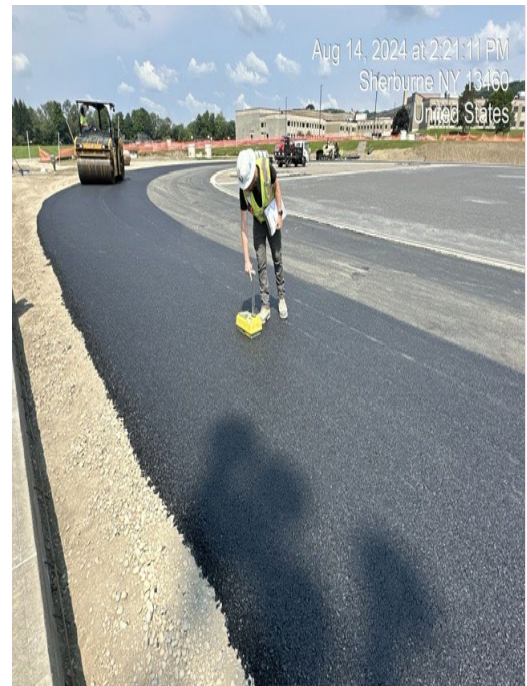

*ATL Onsite for Paving Testing*



*Turf Install Begins*

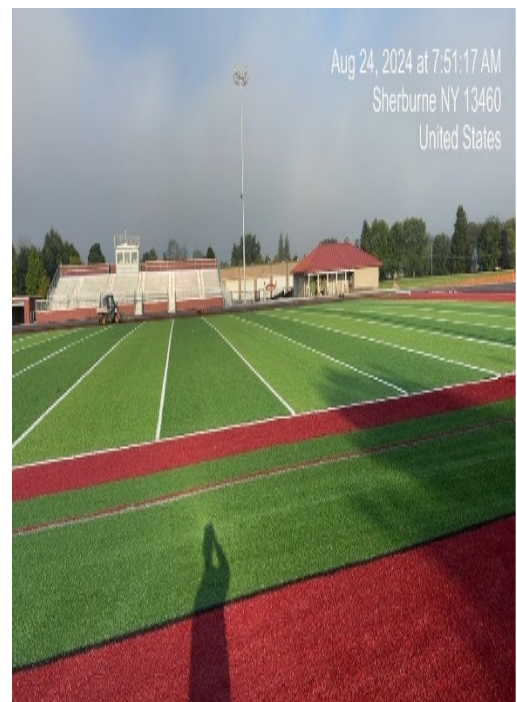


*All Turf Sections Sewn Together*

## Field Progress Photos Continued



*Discus Throwing Pad Poured*

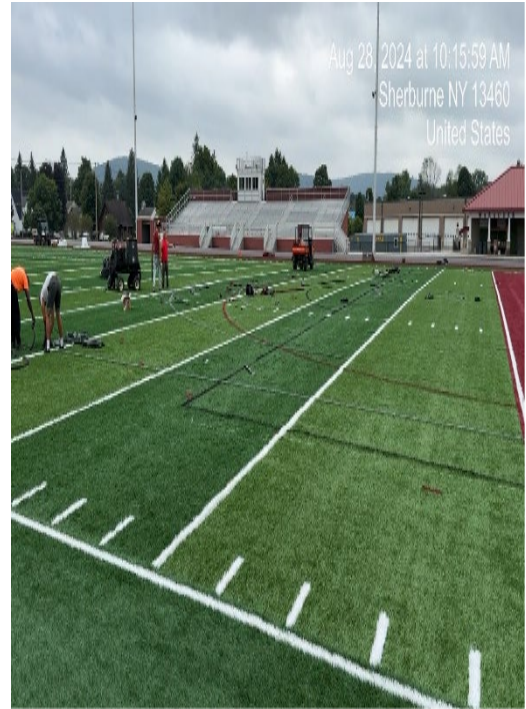

*Turf Field Markings Being Cut In*



*Current View of Construction*
